Knife River
East 2nd Street Reconstrution
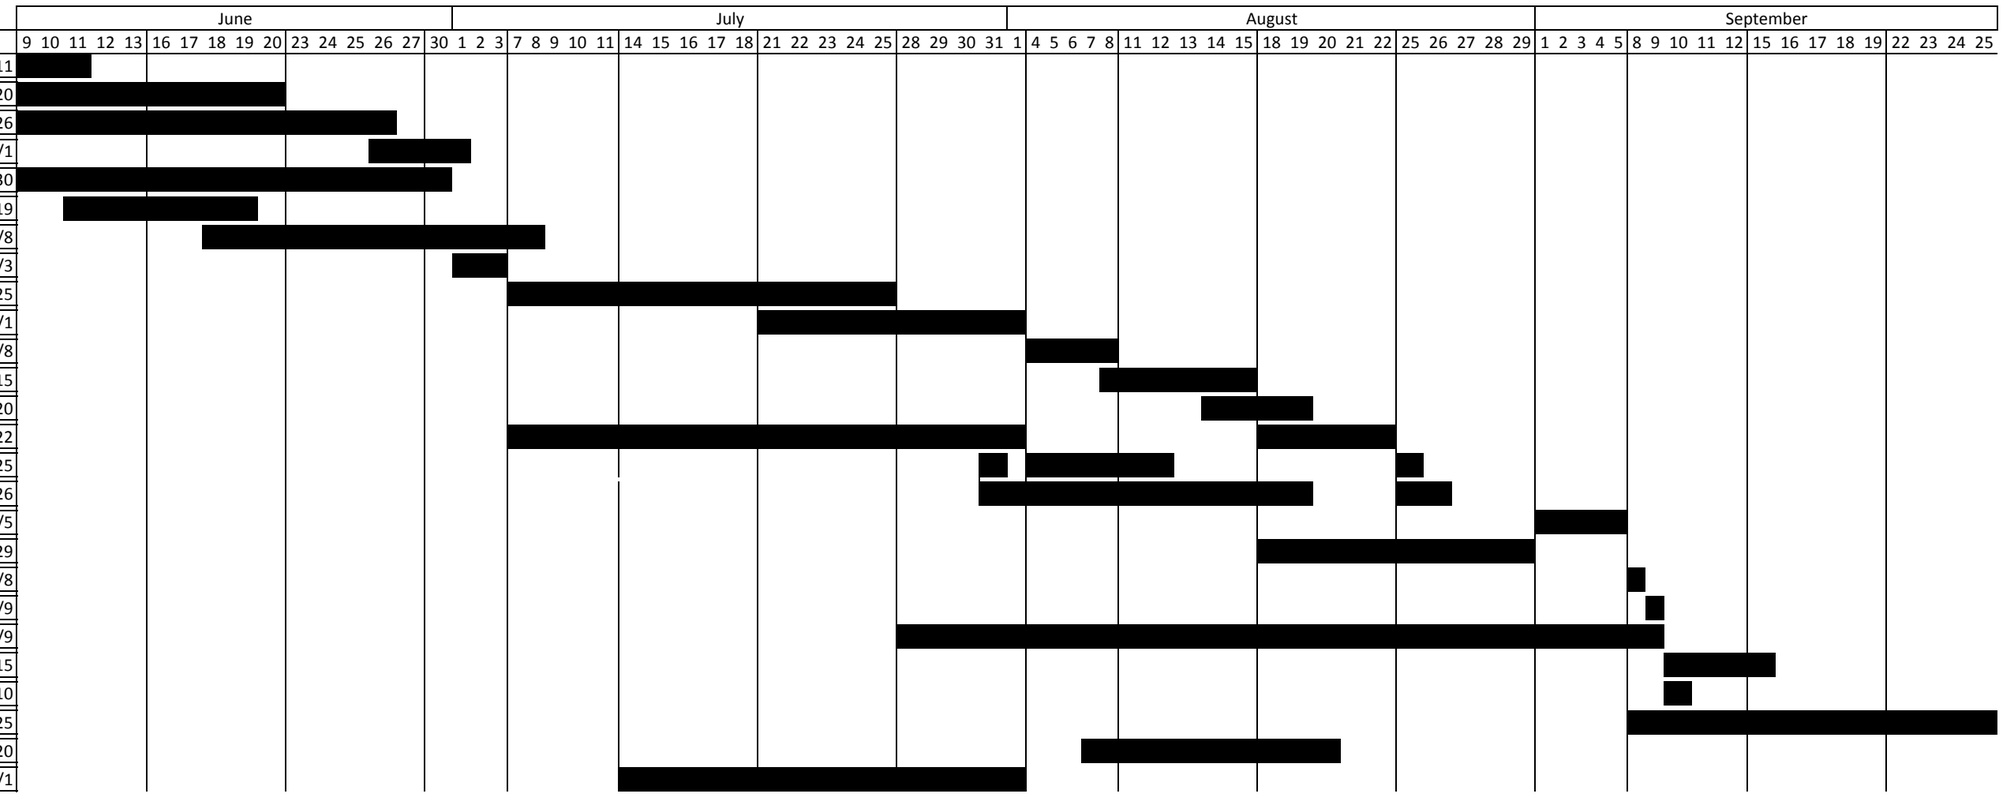
Item	Duration	Start	Finish
Rotomilling	3	6/9	6/11
Muck Excavation	4	6/9	6/20
Rock Embankment	5	6/9	6/26
Uncrushed Sub-Base	4	6/26	7/1
Wetland Mitigation	3	6/9	6/30
Sanitary Sewer West	7	6/11	6/19
Sanitary Sewer East	14	6/18	7/8
Temp Water	3	7/1	7/3
Water	15	7/7	7/25
Storm Drain East	10	7/21	8/1
Cow Creek Sanitary Sewer	5	8/4	8/8
Cow Creek Box Culvert	6	8/8	8/15
Storm Drain West	4	8/14	8/20
Site Prep/Grading	25	7/7	8/22
Fabric	8	7/31	8/25
Crushed Base Course	14	7/31	8/26
Asphalt Paving	5	9/1	9/5
Curb & Gutter	10	8/18	8/29
Median Curb	1	9/8	9/8
Median Cap	1	9/9	9/9
Sidewalk	32	7/28	9/9
Signs	4	9/10	9/15
Striping	1	9/10	9/10
Landscaping	15	9/8	9/25
Area 1 Closure	14	8/7	8/20
Area 3 Closure	21	7/14	8/1
